Lotem® 400 / Lotem 400 Quantum Operator Maintenance

Every 1-2 Weeks

	Part	Work to be done	Completed	Next Maint. Date
1	Air pressure unit	Inspect		
2	Drum vacuum holes	Clean		
3	Drum surface	Clean		
4	Edge detection strip	Clean		
5	Fiber head lens (Fiber head only)	Clean		
6	Loading tray	Clean		
7	Loading wheel	Clean		
8	UDRC hose	Check for cracks		
•	General inspection			

Every 2 Months

	Part	Work to be done	Completed	Next Maint. Date
9	Cooling unit filter (Quantum only) (55-0700)	Replace		


Every 6 Months

	Part	Work to be done	Completed	Next Maint. Date
1	Air pressure filters (518-00630A)	Replace		
10	UDRC filter (57-8792)	Replace		








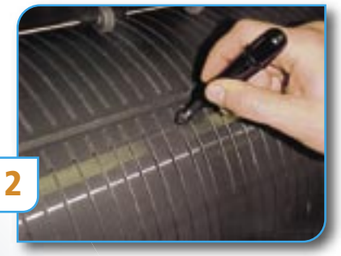








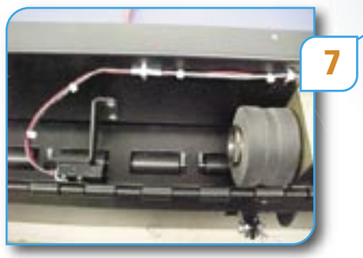





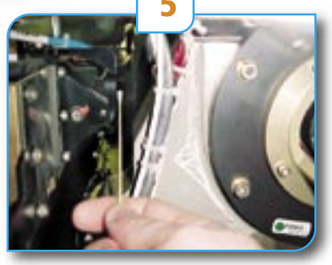

For detailed procedures, see the *Lotem 400 Family / Lotem 400 Quantum Family Maintenance Guide for User*, available on https://ecentral.creo.com

©2005 Creo Inc. All rights reserved. 650-00365B-EN
